

CAPITAL PROJECTS REPORT

JANUARY 2026

MORRISVILLENC.GOV

TABLE OF CONTENTS



5	OVERVIEW	13	INTERNATIONAL DRIVE SIDEWALK GAP
6	PROJECT PAGES KEY	14	LOUIS STEPHENS DR SIDEWALK GAP
8	AIRPORT BLVD EXTENSION	15	SORRELL GROVE CHURCH RD SIDEWALK GAP
9	MORRISVILLE PARKWAY IMPROVEMENTS	16	TOWN CENTER PHASE 1A
10	PUBLIC WORKS FACILITY	18	TOWN CENTER DISTRICT
11	SAWMILL CREEK	20	MORRISVILLE SENIOR CENTER EXPANSION
12	CHURCH STREET SIDEWALK GAP	21	THE GABLES ROADWAY PROJECT

TABLE OF CONTENTS



22	PUBLIC SAFETY MUNICIPAL SERVICES BUILDING	30	FIRE STATION NO. 2 RELOCATION
23	AVIATION PARKWAY SIDEWALK	31	WAKE CO. CONVENIENCE CENTER
25	WCPSS CEDAR FORK ELEMENTARY	33	NCDOT FUTURE ROADWAY PROJECTS
26	NCDOT MCCRIMMON WIDENING/FLYOVER	34	NCDOT AVIATION PARKWAY WIDENING
27	NCDOT NC 54 WIDENING	35	SIDEWALK GAP ASSESSMENT
28	SAVANNAH SUBDIVISION	36	MASTER PLAN - PARKS, RECREATION & CULTURAL RESOURCES
29	WAKE TECH PARK - WATKINS ROAD	37	INTERSECTION IMPROVEMENTS - FUTURE

TABLE OF CONTENTS



38

COMMUNITY CENTER

39

MARCOM DRIVE PARKLAND

40

GLOSSARY



OVERVIEW

Welcome to the Town of Morrisville’s Monthly Capital Projects report. This report is provided so that our residents, businesses, and other stakeholders can easily access information related to capital projects that the Town is undertaking to improve our community and to enhance the Morrisville experience. The Town Council and Town staff are committed to transparency in all that we (and the taxpayer funds we expend) accomplish in and for Morrisville.

This report will be updated once a month, typically on the third Friday of each month, to ensure that the information we are sharing is current. This report is available on the Town website, will be shared via our weekly “Next Week in Morrisville” newsletter ([sign up here](#)) and via our social media platforms. This report will also be provided to Town Council on a quarterly basis so Council can have the opportunity to ask questions and discuss progress on our various projects.

This report addresses current and future Town capital projects that are being designed, constructed, or otherwise studied. However, it does not address all projects from the Town’s five-year Capital Improvement Plan. Some of those projects are not funded and others have not yet moved to an active project. It is also important to focus on the type of project, as many projects start only as design efforts because that is typically funded separately in order to get to a reliable project cost estimate.

This overview page is intended to provide readers with an overview of the content of the report, how capital projects proceed in Morrisville, who we often work with (and why), and how projects are funded.

PROJECT PAGES



Project Manager - This is the point of contact for the project on behalf of the Town.

- START DATE:**
- CURRENT PHASE:**
- COMPLETION DATE:**
- PROJECT MANAGER:**

Project Numbers – this is the current cost estimate for the project and is subject to change as the project evolves and ultimately moves to construction.

- The majority of the Town’s capital projects are funded through the Capital Improvement Plan and various funding methods that include capital reserve funds, re-investment of Parks-Payment-in-Lieu and Streets-Payment-in-Lieu (funds collected from ongoing private development), grant funding, and/or bond funding (voter approved spending).
- In many cases, the Town will pay a portion of a project if partnering with other government entities such as CAMPO, NCDOT, or Wake County. In some cases, the Town will provide funds up front to expedite projects with that funding repaid once the project is complete.

Current Project Phase – highlights the phase each project is currently in; the typical phases include:

- Study/Planning - an initial early planning level exercise to determine project viability, initial scoping and costs. This phase comes before any design work and normally happens before the project is fully developed as a funded capital project and therefore may not be listed in the Town’s 5-year CIP Plan;
- Design (plans are developed to 30% Conceptual, 60% Schematic, 90% Design Development, and 100% Construction Documents with each step normally providing a revised cost estimate);
- Right-of-way/Easement acquisition (many projects require access onto private property, via land acquisition or easement, to use land, often for public infrastructure projects like roads, sidewalks, greenways, drainage, etc);
- Permitting – the Town is required to obtain permits for our projects just as we expect anyone from the public to do;
- Construction – work has begun to construct the project.

- FINANCES**
- Total Revenues & Sources**
\$
- Latest Indicated Cost**
\$

PROJECT PAGES



Project Photo - a current look at the latest phase of each project.

Project Summary - provides a basic overview of the project scope, location and general information about the project.

Strategic Plan Alignment – this shows how the project aligns with the Town’s current Strategic Plan goals and objectives.

Project Status – there are any number of factors that can change or delay a Town project schedule; these include (but are not limited to) the following:

- Challenges with the site materials (particularly the amount of rock found underground in Morrisville) or other site issues that result in unplanned delays.
- Cost increases for materials and for design and construction services.
- Material delays, a much more common challenge in recent years.
- Project partners – in cases where the Town does not manage the project, we are reliant on outside partners, such as NCDOT, and any changes they make to the schedule.
- Interruption of funding, particularly from the federal government.

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

NCDOT AIRPORT BLVD EXTENSION PHASE I



SUMMARY

Design and construction of new roadway segment (0.44 miles) which includes a 4-lane divided roadway with median, streetlights, sidewalks, pedestrian crossings, and new traffic signals from Garden Square Lane to Church Street. This is an NCDOT managed project.

The current cost estimate for all phases of the project is \$15.2 million with the Town's share (inclusive of sunk and future costs) being \$7.2 million.

FINANCES

Total Revenues & Sources
\$7,214,035

Latest Indicated Cost
\$7.2 million

CURRENT STATUS

- The overall project is at 100% design and the project construction let (bid) date is anticipated to be February 2026.
- Utility relocations were completed at the end of December 2025.
- Municipal Maintenance Agreement has been executed. Detour signage for the Indian Creek Greenway has been approved.

Challenges:

- The Town will not know its exact cost share until the project is complete.
- The Town requested a review of the 45 mph speed limit. NCDOT will review after the project is complete when a speed study can be performed.

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

CONSTRUCTION START DATE: APRIL 2026

CURRENT PHASE: DESIGN/ROW/UTILITY RELOCATION

EST. COMPLETION DATE: FEBRUARY 2028

PROJECT MANAGER: TIM JOHNSON, PE

MORRISVILLE PARKWAY IMPROVEMENTS



SUMMARY

Various intersection improvements along Morrisville Parkway from Davis Drive to NC54 as identified in the Access Management plan. Project scope includes new traffic signals, turn lanes, median modifications, striping and pedestrian safety improvements. Project is currently authorized for design phase only. Current phase improvements and Latest Indicated Cost are limited to the intersections between Davis Drive (except for a westbound right turn lane) and NC 54 (Chapel Hill Road).

STATUS

- 65% design plans and cost estimate are complete and are being reviewed by NCDOT.
- CAMPO LAPP application submitted for Right of Way and Utility funding and CAMPO recommended funding in the amount of \$205,030 for FY27. The proposed work plan has been phased to align with the Town's budget capabilities. LAPP funding is a key component for future phases as the project is currently authorized for design only.

Challenges:

- NCDOT was requested to perform a traffic study at Morrisville Elementary, however, NCDOT was unable to perform due to workload. In response, the Town has completed a school traffic study.
- Working with NCDOT and the Town of Cary as potential project funding partners.

FINANCES

Total Revenues & Sources
\$1,658,000

Latest Indicated Cost
\$6.8 million. Town share = \$1.4 million

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: OCTOBER 2024

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: TBD

PROJECT MANAGER: TIM JOHNSON, P.E.

PUBLIC WORKS FACILITY



SUMMARY

Purchase of an existing building at 125 International Drive to be renovated for a replacement public works facility.

\$10.5 million authorized for purchase, due diligence, and engineering.
\$10.0 million anticipated for renovations and upfit of the building.

FINANCES

Total Revenues & Sources
\$20.5 million

Latest Indicated Cost
\$20.2 million

STATUS

- Closed on property on July 10, 2025.
- Council authorized the Design-Build delivery method for the rehabilitation of the building to accommodate Public Works.
- Town Council approved the Phase 1 Design Services contract with Balfour Beatty and the design phase is currently underway.
- Early construction phase contract with Balfour Beatty including demolition and site work planned for February Council review.

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: MARCH 2025


CURRENT PHASE: PROGRAMMING/DESIGN

EST. COMPLETION DATE: 2027

PROJECT MANAGER: TIM JOHNSON, P.E.

SAWMILL CREEK

STREAM RESTORATION AND GREENWAY PROJECT

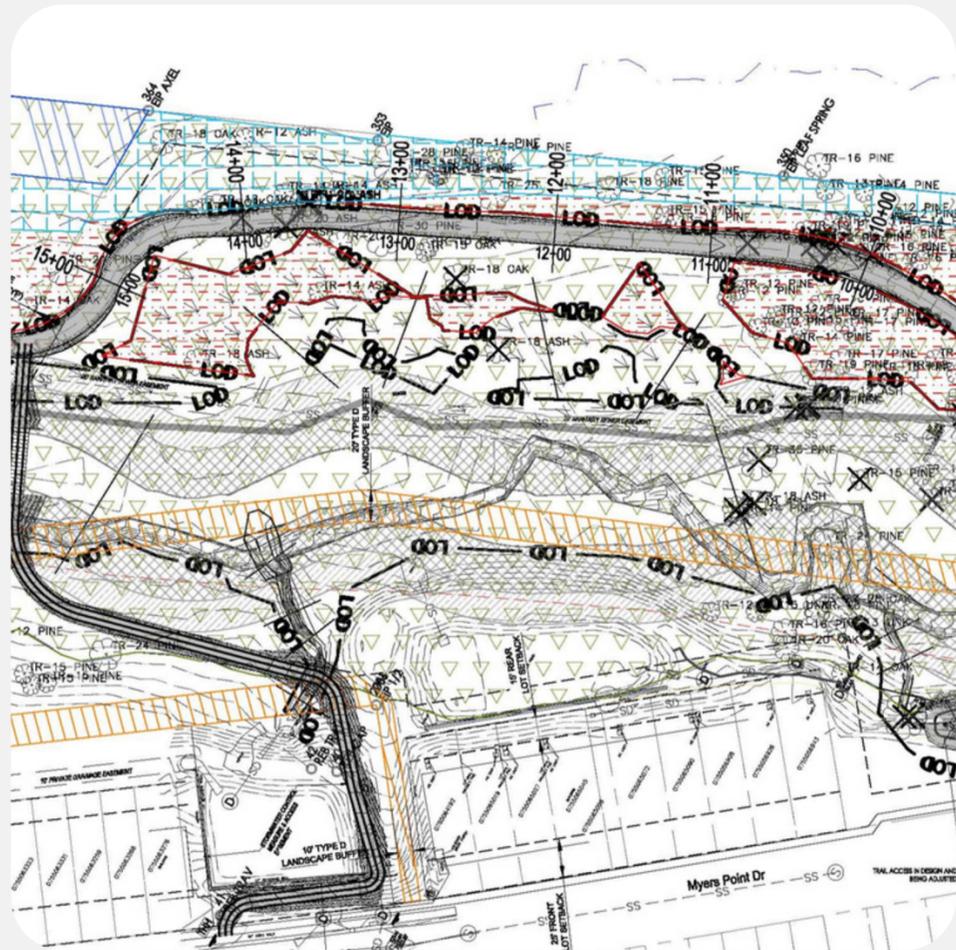

START DATE: JULY 2023

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: 2027

PROJECT MANAGER: BEN MILLS P.E., C.F.M.

SUMMARY

The project is water quality focused and will tackle an unstable stream and poor habitat conditions. The work includes stabilizing the eroding stream, enhancing the riparian buffer by removing invasive species and adding native plantings while incorporating pocket wetlands to help improve water quality and habitat conditions. The development would also incorporate a portion of the planned Sawmill Creek greenway in its design. The project is generally located west of the railroad right-of-way adjacent to NC54 from Page Street to Downing Glenn Drive.

STATUS

- The design is complete and is currently in plan review.
- The Town has been awarded three grants totaling \$967,297 towards project implementation.
- The final plat for the project, which includes obtaining greenway and construction easements, has been approved.
- Additional revenues to be allocated from Stormwater Reserves at time of construction contract award.
- Environmental permitting is complete.

Challenges:

- Differences in elevation and stream crossings necessitate the use of elevated greenway sections and bridges, adding to project costs.
- To meet the conditions of the newly awarded Great Trails Grant, the start of construction will likely be delayed by a couple of months.

FINANCES

Total Revenues & Sources
\$1,840,099


Latest Indicated Cost
\$2,500,000

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

SIDEWALK GAP PROJECT

CHURCH STREET SIDEWALK (EB-5838)

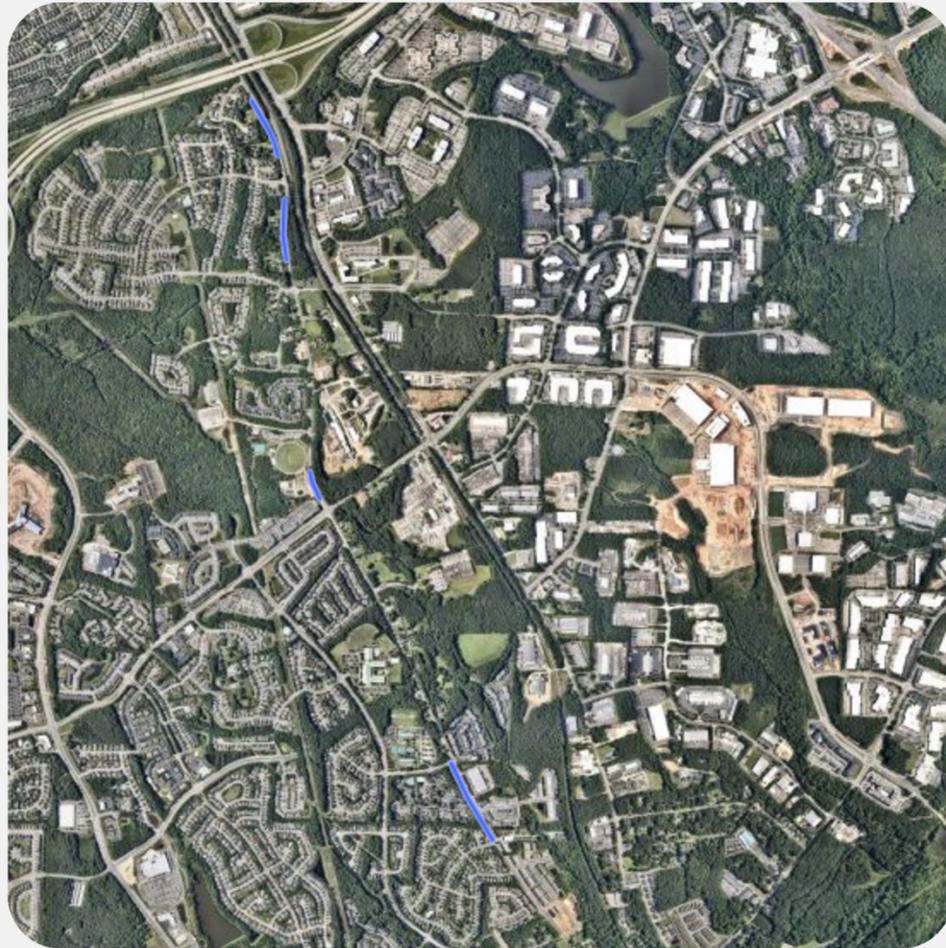

SUMMARY

Design and construct new sidewalks along Church Street from Morrisville-Carpenter Road to the Durham County line. This project is in conjunction with NCDOT and is funded with an 80% State funds/20% Town funds cost share reimbursement grant, managed by the Town.

STATUS

- Comments received from NCDOT review of 65% design plans.
- Revisions on Environmental permitting documents based on NCDOT comments underway.
- Schedule and Cost estimate revisions underway.

Challenges:

- Coordination needed with other projects in the corridor.
- Federal funding availability may require the project to scale back.

FINANCES

Total Revenues & Sources
\$3,058,103

Latest Indicated Cost
\$5.2 million

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: 2022



CURRENT PHASE: DESIGN

EST. COMPLETION DATE: 2027

PROJECT MANAGER: KITTY THOMAS

SIDEWALK GAP PROJECT

INTERNATIONAL DRIVE

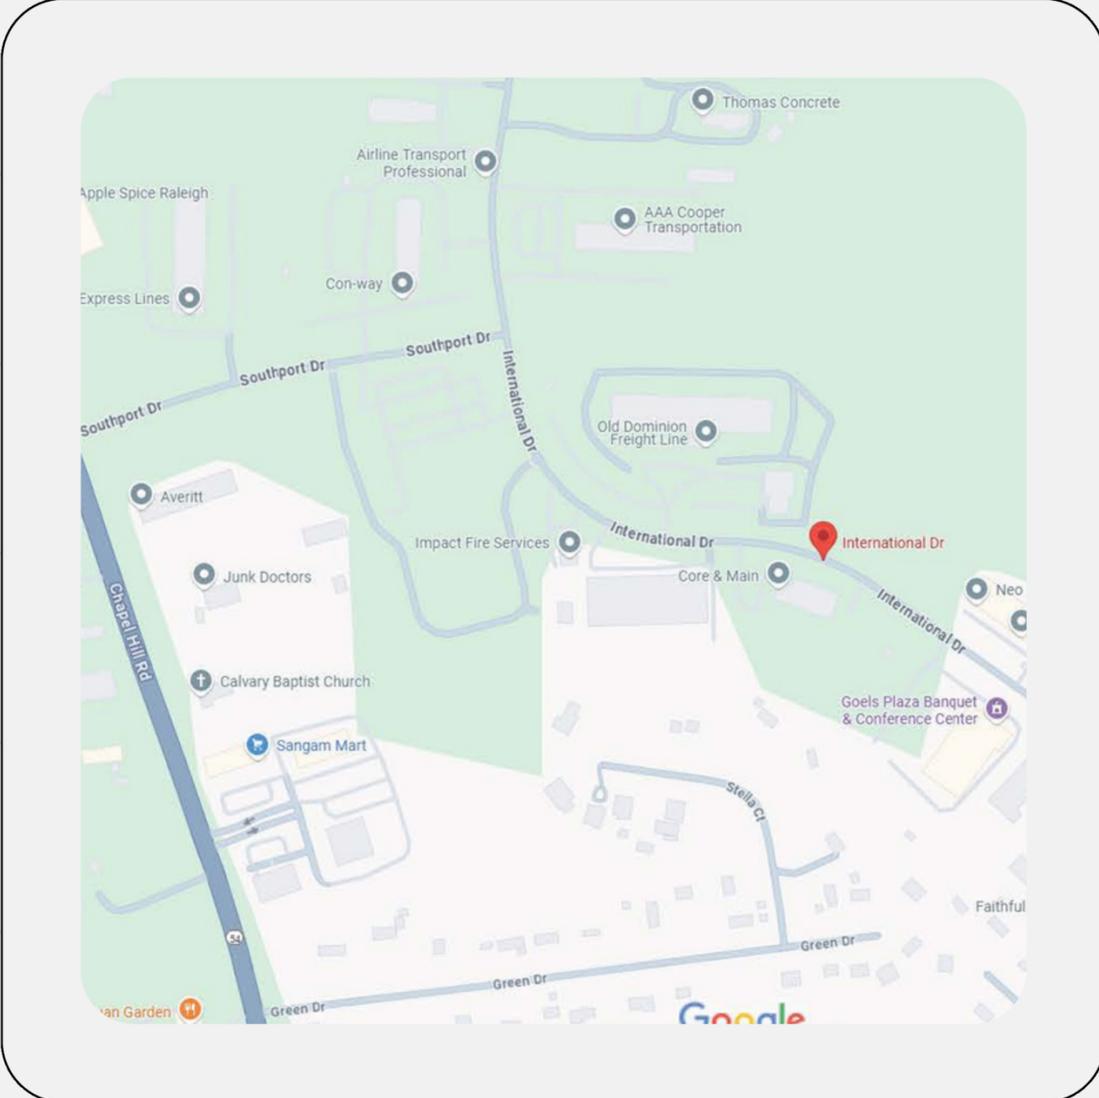

START DATE: OCTOBER 2024

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: 2026

PROJECT MANAGER: TIM JOHNSON, P.E.

SUMMARY

Complete sidewalk gaps on International Drive from Aviation Parkway north to the end of the existing pavement connecting to the proposed roadway alignment being developed by SPARK.

STATUS

- 100% plans are complete.
- The Town's contracted estimating firm has completed the 100% plans construction estimate.
- Anticipate bid advertisement in January/February 2026.
- Additional revenues to be allocated from Transportation Reserves at time of construction contract award.

Challenges:

- Duke Energy poles need to be relocated.
- Town of Cary permits must be clarified.

FINANCES

Total Revenues & Sources
\$891,000


Latest Indicated Cost
\$1.5 million

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

SIDEWALK GAP PROJECT

LOUIS STEPHENS DR (BL-0049)

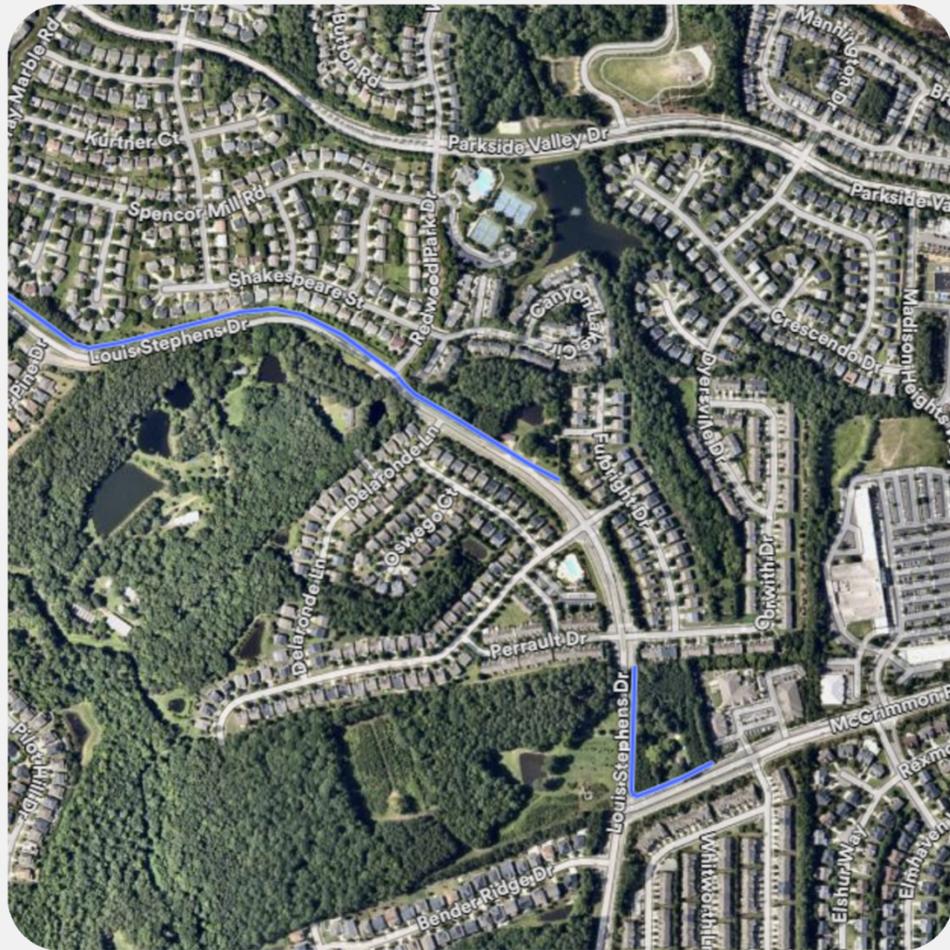

SUMMARY

Design and construction of a new sidewalk along Louis Stephens Drive from McCrimmon Parkway to Parkside Valley Drive. This project is in conjunction with NCDOT and is funded with an 80% State funds/20% Town funds cost share reimbursement grant, managed by the Town.

STATUS

- Design phase underway. The final plans are in NCDOT review.
- Right of Way (ROW) acquisitions continue with easements on only one out of five parcels remaining to be acquired, for which a settlement agreement is being processed.
- Revision of Environmental documents as needed is underway.
- Revised cost estimate and discussion on additional funding request underway.

Challenges:

- Potential habitat for endangered species.
- Variances needed on the NCDOT standard specifications.
- ROW negotiations require condemnation of several parcels.

FINANCES

Total Revenues & Sources
\$2.4 million

Latest Indicated Cost
\$2 million

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: OCTOBER 2022

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: 2026

PROJECT MANAGER: KITTY THOMAS

SIDEWALK GAP PROJECT

SORRELL GROVE CHURCH ROAD



SUMMARY

Sorrell Grove Church Road sidewalk gap from Airport Boulevard to Slater Road was identified in the sidewalk gap prioritization schedule. A new sidewalk is being designed to be constructed on the west side of Sorrell Grove Church Road.

STATUS

- Stakeholder review on 90% design plans for sidewalk completed. NCDOT review and encroachment permit process underway.
- State and County environmental permit applications are still under review.
- Additional revenues to be allocated from Transportation Reserves at time of construction contract award.

Challenges:

- Long review times for State permits.

FINANCES

Total Revenues & Sources
\$332,000

Latest Indicated Cost
\$1.3 million

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency


START DATE: OCTOBER 2024

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: 2026/2027

PROJECT MANAGER: KITTY THOMAS

TOWN CENTER PHASE 1A

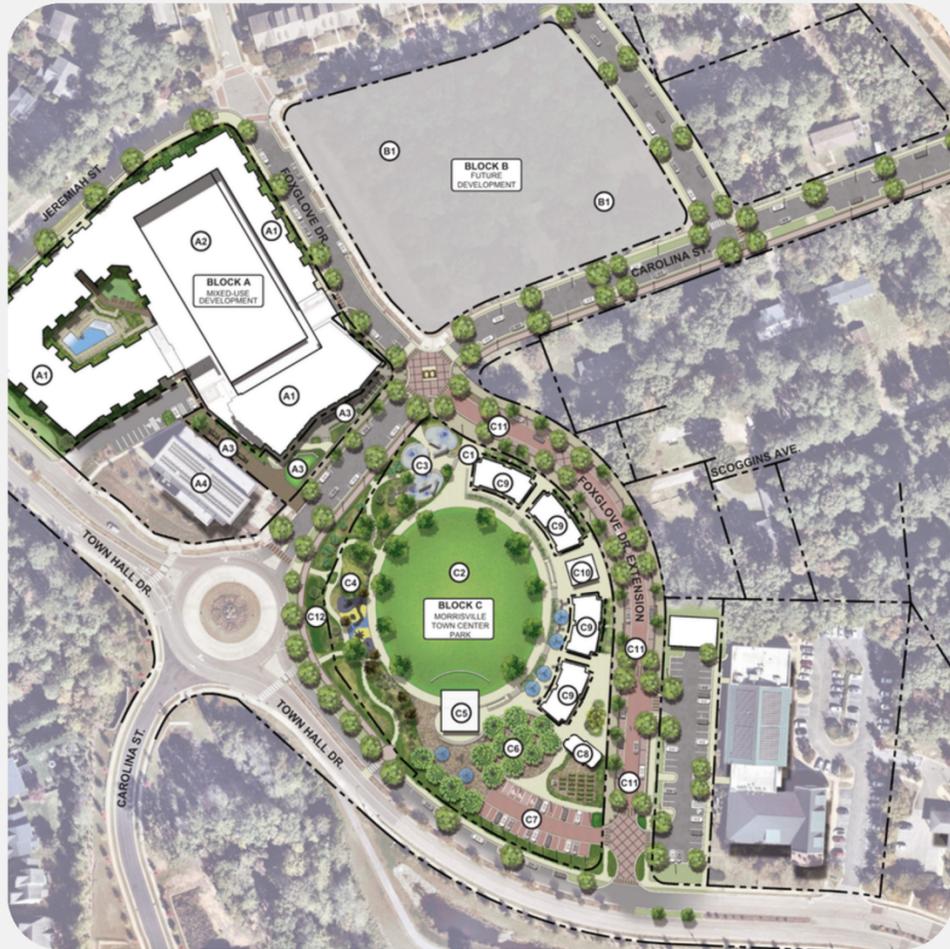

START DATE: SUMMER 2024

CURRENT PHASE: CONSTRUCTION

EST. COMPLETION DATE: 2027/2028

PROJECT MANAGER: KYLE COOPER

SUMMARY

Block A comprises of a mixed-use building and a parking deck surrounding the existing library. Block C comprises of a new town green, outdoor stage, cottage retail buildings, public restroom, plaza with sculptures and water features, walkways, new streetscapes along Town Hall Drive, Foxglove and Carolina Street, playground and landscape/hardscape features throughout.

STATUS

- Block A plans have been submitted for plan approval:
 - Package 1 – Mixed Use Building – review complete
 - Package 2 - pocket park and temp parking lot – review complete
 - Library temporary parking lot construction has commenced/
- Block C (Town Green) - Construction has commenced, construction fence has been installed around Block C, demolition and site work have commenced. Building permits under review for stage, restroom, trash building and retail units.

Challenges:

- Designing the park amenities within the allocated budget.

FINANCES

Total Revenues & Sources
\$30,874,349

Latest Indicated Cost - Design + Construction
\$28.8 million

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency



HIGHLIGHTS



TOWN CENTER PHASE 1

TOWN CENTER DISTRICT

BRANDING, SIGNAGE AND WAYFINDING PLAN



SUMMARY

Develop a town center district branding, signage and wayfinding program in connection identifying key points of interest like the Town Green, library, playgrounds, dog park, retail centers, historic landmarks and other locations. Project master plan will include implementation of street level and pedestrian level signs, establishing a complementary, yet unique Town Center District brand.

STATUS

- The Town has selected and contracted with Merje to provide signage, branding and wayfinding consulting services for Town Center. The consultant team has visited the area and meet with stakeholders to gather preliminary information.
- The master plan will provide a phased implementation and funding plan.
- Initial presentation and input gathering session with Town Council took place on January 13, 2026.
- Follow-up presentation to Council for branding/wayfinding update planned for summer 2026.
- Completion date of 2027/2028 includes implementation.

FINANCES

Total Revenues & Sources
\$99,945

Latest Indicated Cost
\$99,945

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: NOVEMBER 2025

CURRENT PHASE: PLANNING

EST. COMPLETION DATE: 2027/2028

PROJECT MANAGER: JEANNE HOOKS





HIGHLIGHTS



EXISTING MONUMENT SIGN

EXISTING WAYFINDING SIGN

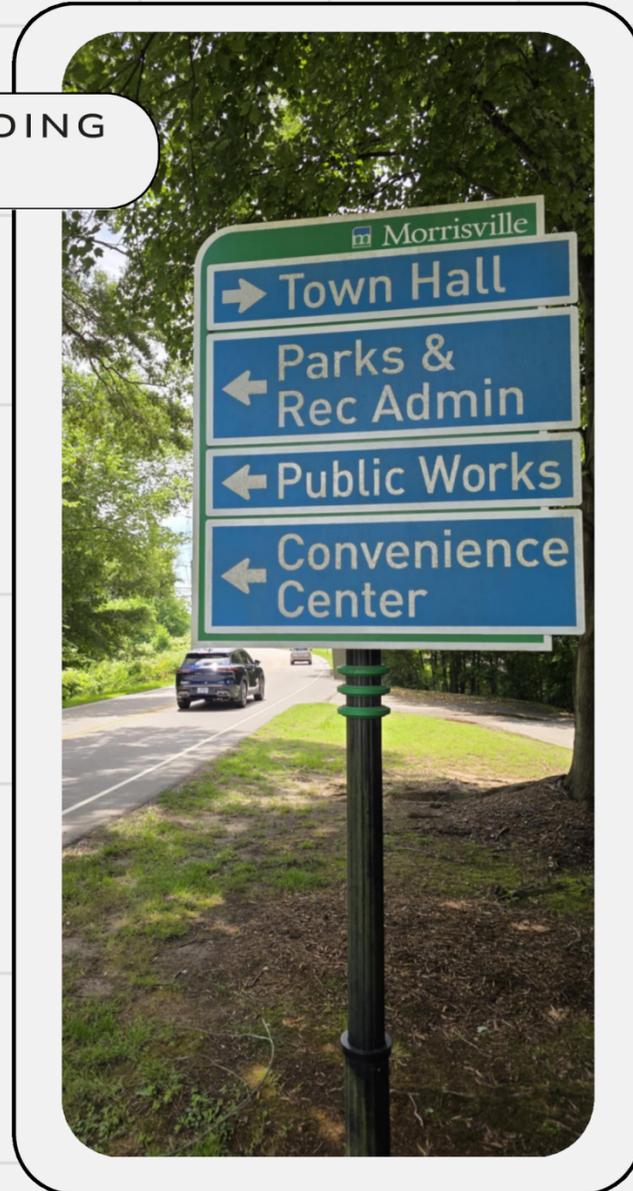

TOWN CENTER DISTRICT BRANDING, SIGNAGE AND WAYFINDING



TOWN CENTER DISTRICT CONCEPTUAL PLAN

MORRISVILLE SENIOR CENTER EXPANSION



SUMMARY

Expand into two additional store frontage spaces adjacent to the existing Senior Center at the McCrimmon Corners shopping center bringing the total space available to approximately 5,500 SF. This will provide additional programming space to accommodate the interests of the patrons.

STATUS

- Design phase with Design Development plans stakeholder review underway including project construction estimation to verify proposed design meets budget constraints.
- Stakeholder engagement continues. A meeting with the Seniors was held on December 8, 2025.
- A lease amendment was executed to acquire the additional space.

Challenges:

- Phasing of the project will add time and cost.
- Fitting needs and preferences within the current budget.

FINANCES

Total Revenues & Sources
\$850,000

Latest Indicated Cost
\$850,000

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: SUMMER 2025

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: NOVEMBER 2026

PROJECT MANAGER: KITTY THOMAS

THE GABLES ROADWAY PROJECT



SUMMARY

This project is to evaluate the condition of streets in the Gables community and to design and implement repairs and reconstruction solutions to bring the streets up to current town standards.

STATUS

- Development of a Request for Qualifications for Design-Build continues with anticipated advertisement early 2026.
- Additional revenue required will be funded by municipal service district tax and will be allocated at time of contract award.

Challenges:

- The roadway deterioration is unexpected for a roadway network of this age and was a result of poor construction practices when originally constructed.
- Cost escalations have made it more difficult to proceed with construction.
- Right-of-way constraints will create construction challenges

FINANCES

Total Revenues & Sources
\$300,000

Latest Indicated Cost
\$2.6 million

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: DECEMBER 2023

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: 2026

PROJECT MANAGER: KITTY THOMAS

PUBLIC SAFETY/CHAMBER OF COMMERCE

MUNICIPAL SERVICE BUILDING



START DATE: DECEMBER 2025

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: SPRING/SUMMER 2026

PROJECT MANAGER: STEVEN SPRUILL

SUMMARY

Minor building rearrangements to accommodate relocation of Parks and Recreation Administration staff at the Chamber of Commerce building as well as minor improvements to public access for Police, Planning, and Inspections.

STATUS

- Town acquired the Chamber of Commerce suite and now owns/controls the entire commercial building condominium.
- Designer is working with staff departments to develop program requirements and prepare conceptual plans.
- With the acquisition of the Chamber of Commerce building, Parks, Recreation and Cultural Resources administration will be relocating their staff to this location.

Challenges:

- Parking spaces are limited due to construction of Town Center.

FINANCES


Total Revenues & Sources
\$1.125 million

Latest Indicated Cost
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

AVIATION PARKWAY PEDESTRIAN ACCESS

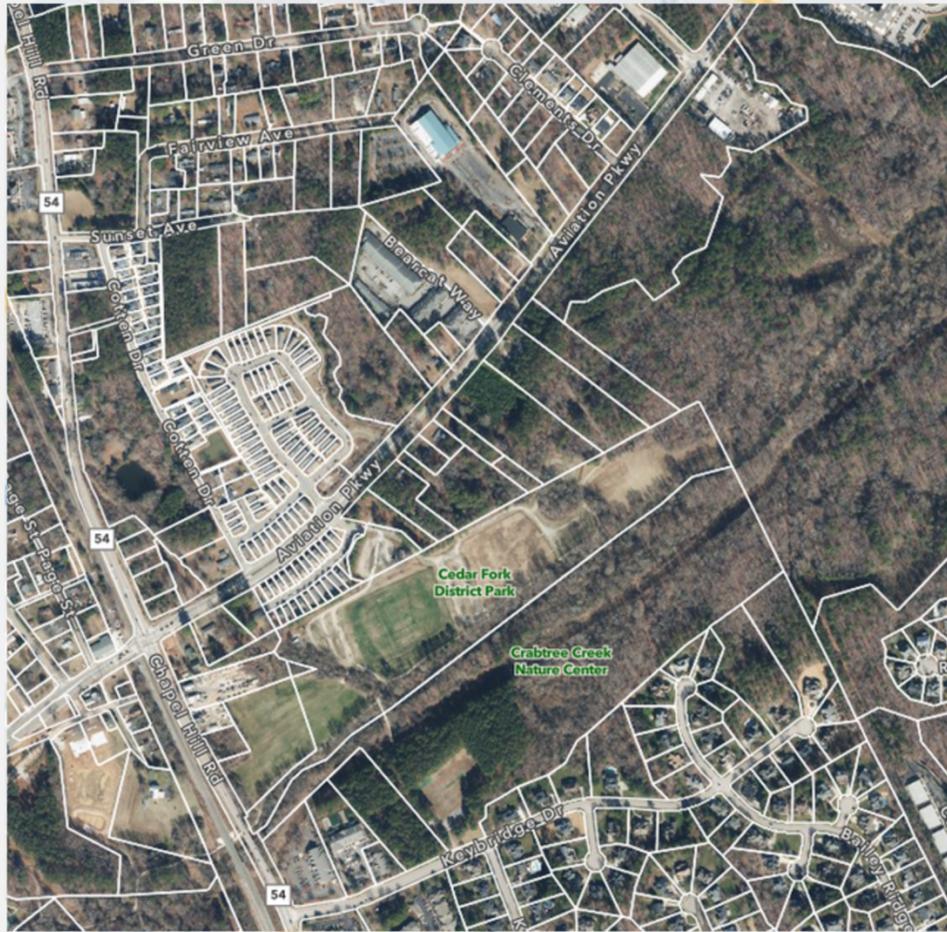

SUMMARY

NCDOT plans to widen Aviation Parkway from NC 54 to I-40. The existing roadway will be widened to a four-lane, median-divided section with bicycle and pedestrian facilities. A quadrant-loop intersection is proposed at the intersection of Aviation Parkway and NC 54, and NC 54 is proposed to be shifted slightly to the east to create greater separation between the railroad and roadway. The Town allocated funds in FY26/27 to advance a pedestrian project to enhance pedestrian safety.

FINANCES

Total Revenues & Sources:
\$1,600,000

Latest Indicated Cost:
\$TBD

STATUS

- The Town is currently updating the Comprehensive Transportation Plan and the Parks Master Plan which will provide guidance to the preferred walking path that will connect Cedar Fork District Park to HSNC possibly along Aviation or along the existing greenway including a crosswalk option to cross from the south to the north side of Aviation Parkway.
- Town is also considering a temporary path option using the existing greenway for special event purposes.

Challenges:

- Extensive coordination with NCDOT and Wake County

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: OCTOBER 2025

CURRENT PHASE: PLANNING

EST. COMPLETION DATE: 2027

PROJECT MANAGER: TIM JOHNSON, P,E,



CAPITAL PROJECTS
FY26-29
FUTURE PROJECTS

WCPSS CEDAR FORK ELEMENTARY

ATHLETIC FIELDS



START DATE: FALL 2025

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: SUMMER 2027

PROJECT MANAGER: MICHELE STEGALL

SUMMARY

New multi-purpose athletics facilities to be constructed in partnership with Wake County Public Schools as part of an Interlocal Agreement with them related to the construction of a new high school to serve the Morrisville high school students. The Town of Morrisville will handle betterments such as sport lighting and the maintenance.

STATUS

- WCPSS hosted a community meeting on August 6, 2025. Staff from Administration, Parks and Planning were in attendance. A total of seven community members were in present. Various questions were asked about lights, noise and hours of operation.
- A site plan application is currently under review by the Town Development Services departments.

Challenges:

FINANCES

Total Revenues & Sources
\$731,000

Latest Indicated Cost
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

NCDOT MCCRIMMON WIDENING/FLYOVER

U-5747



SUMMARY

NCDOT is widening McCrimmon Pkwy from two to four lanes from west of Davis Dr to Perimeter Park Dr. The project includes a flyover over the railroad tracks and NC 54, displaced left-hand turn lane design at Davis Dr, additional improvements at intersections along the roadway segment, street lights, bridge lighting and aesthetic enhancements, on-street bike lanes, and a wider sidewalk/multi-use path on the north side of the roadway. The flyover / bridge is proposed to be named in remembrance of Sergeant Godwin.

STATUS

- Full right-of-way certification is anticipated soon, and the construction let date is currently now scheduled for May of 2027.
- NCDOT is working to produce final cost estimates for Town betterments, and Town staff is anticipating receipt of a draft municipal agreement from NCDOT for betterment engineering services within the coming months to solidify integration of betterments into the overall design for the facility.

Challenges:

- Right-of-way and easement acquisition has been slower than anticipated, resulting in NCDOT delaying the project schedule several times.

FINANCES

Total Revenues & Sources:
\$2,316,764 for Town-financed betterments

Latest Indicated Cost:
\$90.2 million remaining for full project (cost to NCDOT)

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: 2021


CURRENT PHASE: DESIGN/ROW

EST. COMPLETION DATE: 2030

PROJECT MANAGER: BRET MARTIN

NCDOT NC 54 WIDENING

U-5750

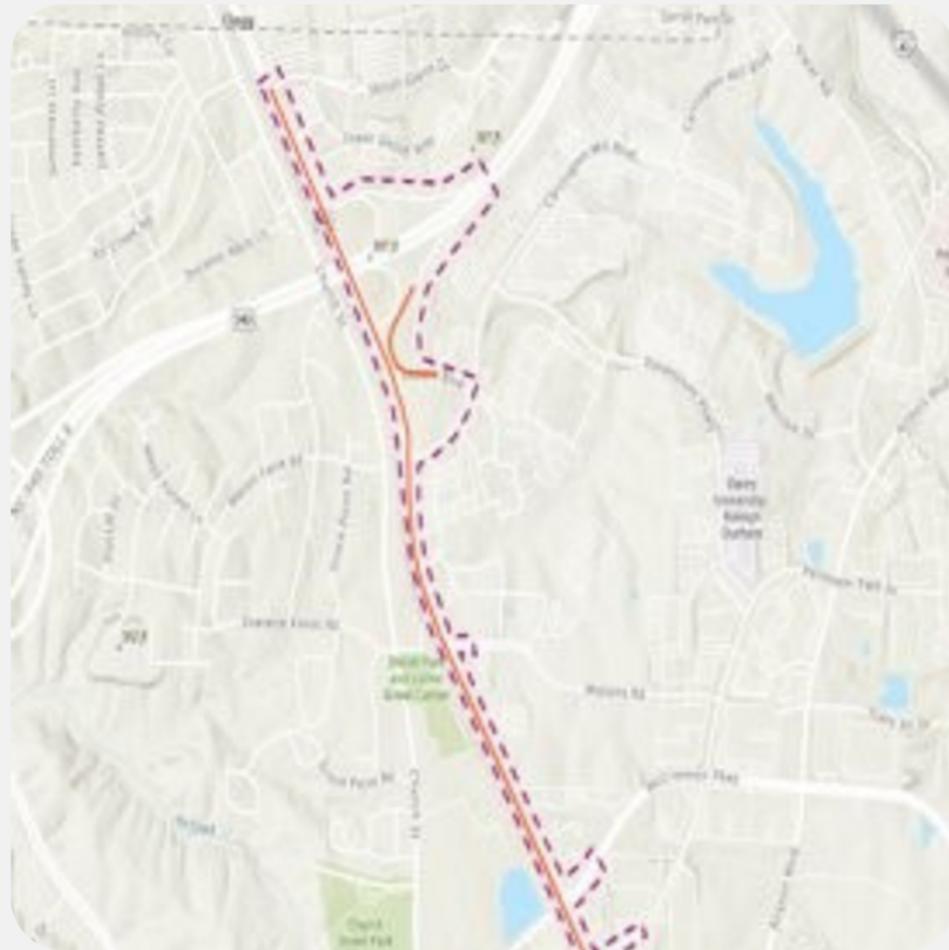

SUMMARY

NCDOT is widening NC 54 from two lanes to four lanes from Shiloh Glenn Drive to Perimeter Park Drive, with additional lanes around the NC 540 interchange. The project includes access management changes along the corridor, streetlights, traffic signal and pedestrian crossing improvements at the Carrington Mill Blvd/Lichtin Blvd intersection, ten-foot multi-use path, and project integration with the McCrimmon Pkwy widening and flyover project (U-5747).

FINANCES

Total Revenues & Sources:
\$594,148 for Town-financed betterments

Latest Indicated Cost:
\$41.1 million remaining for full project (cost to NCDOT)

STATUS

- U-5750 and U-5747 are now planned to be let for construction together in May 2027.
- NCDOT is working to produce final cost estimates for Town betterments, and Town staff is anticipating receipt of a draft municipal agreement from NCDOT for betterment engineering services within the coming months to solidify integration of betterments into the overall design for the facility.

Challenges:

- Right-of-way and easement acquisition has been slower than anticipated for the McCrimmon Pkwy widening project, resulting in NCDOT moving both project schedules out several times.

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: 2021

CURRENT PHASE: DESIGN/ROW

EST. COMPLETION DATE: 2030

PROJECT MANAGER: BRET MARTIN

SAVANNAH SUBDIVISION

CULVERT UPGRADE



SUMMARY

Design and construction of drainage system upgrades to eliminate flooding that occurs at the Old Savannah Subdivision along Star Magnolia and Morrisville Carpenter Road during high storm events.

STATUS

- Study phase has been completed.
- Planned start of design scheduled for FY 27.

Challenges:

- Disrupting Morrisville Carpenter Road with a potential underground pipe crossing and developing options to minimize this conflict.

FINANCES

Total Revenues & Sources
\$1,750,000

Latest Indicated Cost
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: FY27 (DESIGN)

CURRENT PHASE: FUTURE

EST. COMPLETION DATE: TBD

PROJECT MANAGER: BEN MILLS, P.E.

WAKE TECH PARK - WATKINS ROAD



SUMMARY

Design and construction of a new passive park with parking and a restroom/shelter building.

FINANCES

Total Revenues & Sources
\$6,050,000

Latest Indicated Cost
\$TBD

STATUS

- Planned start of design in FY 26.
- Programming to be an outcome of the Parks Master Plan update.

Challenges:

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: FY26/27

CURRENT PHASE: FUTURE

EST. COMPLETION DATE: TBD

PROJECT MANAGER: TBD

FIRE STATION No. 2 RELOCATION



SUMMARY

Design and construction of a new fire station to replace the current fire station #2. NCDOT will be widening NC54 at the location of existing fire station #2 which will impact its operational use as a fire station. Wake Tech has provided land along Paramount Parkway for Town's use as the future fire station #2 location which will enhance service in the NE region of the Town's fire safety service area.

STATUS

- Planned start of design in FY 27 as a design build project .
- Station will be designed with the general program parameters that were developed for Fire Station #3 which was completed in 2023 on Harris Mill Road.

Challenges:

FINANCES

Total Revenues & Sources
\$14,800,000

Latest Indicated Cost
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: FY27/28

CURRENT PHASE: FUTURE

EST. COMPLETION DATE: TBD

PROJECT MANAGER: TBD

WAKE COUNTY CONVENIENCE CENTER

SOLID WASTE FACILITY



START DATE: 2025 (RE-START)

CURRENT PHASE: PRELIMINARY DESIGN

EST. COMPLETION DATE: TBD

PROJECT MANAGER: TBD

SUMMARY

With the termination of the joint Western Wake Convenience Center and Public Works Facility, Wake County is reviewing options for a stand-alone Solid Waste Facility. One option is to have the facility on Aviation Parkway were the joint facility was planned.

This project is funded and managed by Wake County with a proposed land partnership with the Town of Morrisville.

STATUS

- On August 12, 2025 Town Council passed resolution 2025-283-0 authorizing the Town Manager to execute the Fifth Amendment to the Memorandum of Understanding with Wake County for the development of a new Solid Waste Convenience Center on Town owned property located at 414 Aviation Parkway to be developed, operated and funded by Wake County.
- Additional agreements will be required prior to construction.

Challenges:

- A new Special Use Permit will be required.
- Public Works will need to vacate it's current facilities and move into the 125 International Drive facility to enable the county to proceed with construction of the new convenience center.

FINANCES

Total Revenues & Sources
\$TBD

Latest Indicated Cost
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency



FUTURE PROJECT PLANNING/STUDIES

NCDOT FUTURE ROADWAY PROJECTS



SUMMARY

Various NCDOT roadway projects planned/programmed to be implemented in Morrisville in the next 10 years. The latest indicated costs are costs to NCDOT and not the Town.

FINANCES

Total Revenues & Sources:
\$TBD

Latest Indicated Cost:
\$TBD

STATUS

- Draft 2026-2035 STIP – The draft of the State Transportation Improvement Program (STIP) for 2026-2035 has been adopted by the North Carolina Board of Transportation. The STIP identifies funding for transportation project construction and other associated activities, costs, and schedules for projects throughout the state over a 10-year period.
- The Capital Area Metropolitan Planning Organization (CAMPO) Executive Board adopted its 2026-2035 TIP to match the new STIP at its August regular meeting.
- CAMPO has submitted projects for scoring through NCDOT’s SPOT 8.0 prioritization process that will inform the next major STIP update for FYs 2028-2037.

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: TBD


CURRENT PHASE: CONCEPTUAL

EST. COMPLETION DATE: TBD

PROJECT MANAGER: BRET MARTIN

NCDOT AVIATION PARKWAY WIDENING

U-5811

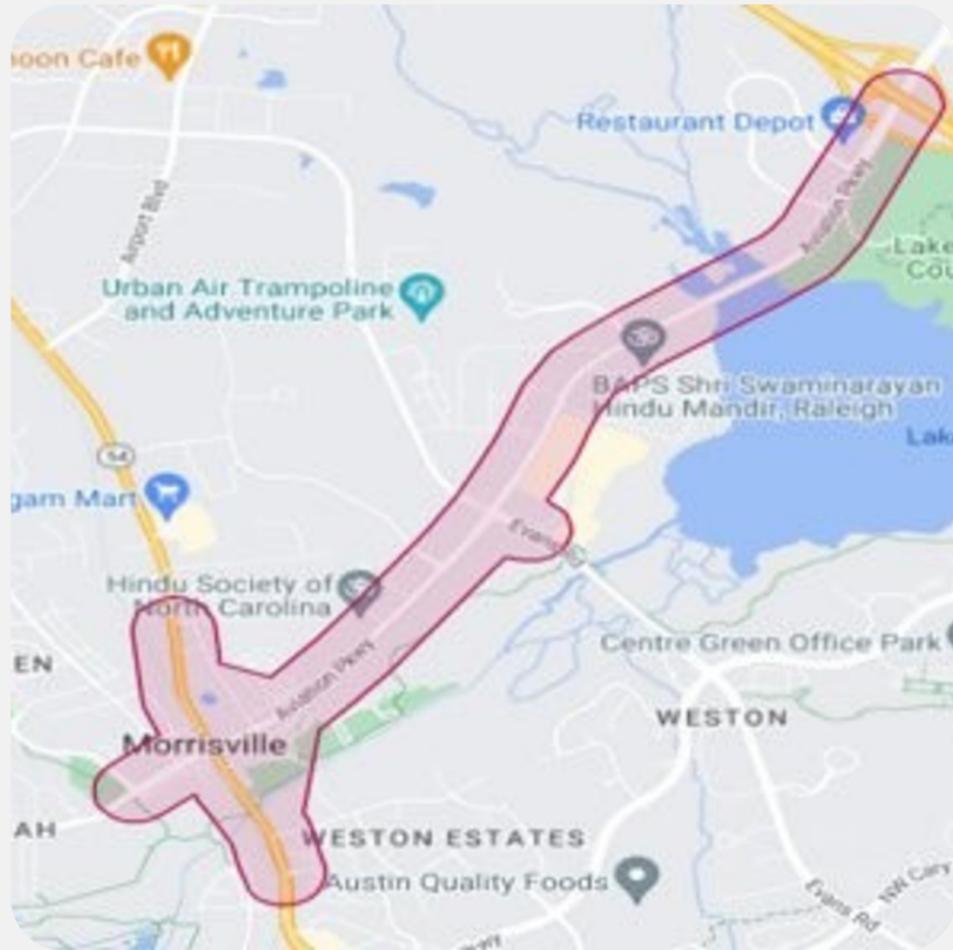

FINANCES

Total Revenues & Sources:
\$TBD

Latest Indicated Cost:
\$67.3 million
remaining for project

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

SUMMARY

NCDOT plans to widen Aviation Parkway from NC 54 to I-40. The existing roadway will be widened to a four-lane, median-divided section with bicycle and pedestrian facilities. A quadrant-loop intersection is proposed at the intersection of Aviation Parkway and NC 54, and NC 54 is proposed to be shifted slightly to the east to create greater separation between the railroad and roadway. The purpose of this project is to address congestion issues through 2050, to improve east-west mobility through Morrisville, and improve operations at intersections.

STATUS

Aviation Parkway Widening (NC 54 to I-40) (U-5811):

- A conceptual functional design for the project is complete. ROW plans are being developed.
- A public meeting was held by NCDOT on May 12th to gather feedback on the conceptual functional design for the project before proceeding with more detailed design and other implementation planning efforts.
- Town staff is currently working with NCDOT to consider various signalization and pedestrian treatments for the facility.

Challenges:

- The draft STIP shows the Aviation Parkway widening (U-5811) project starting construction in FY30.

START DATE: 2025 (RE-START)

CURRENT PHASE: PRELIMINARY DESIGN

EST. COMPLETION DATE: 2032

PROJECT MANAGER: BRET MARTIN

SIDEWALK GAP ASSESSMENT



SUMMARY

Perform a physical survey/inventory of sidewalks adjacent to all streets/roads within Morrisville’s Planning Jurisdiction including NCDOT maintained streets/roads to gather data that will be incorporated in the Town’s GIS database.

FINANCES

Total Revenues & Sources
\$16,000

Latest Indicated Cost
\$36,000

STATUS

- Initial study of sidewalk gaps and inventory is complete.
- Selecting a firm to recommend prioritization process and updated criteria.

Challenges:

- The next steps are potential updating of sidewalk criteria and prioritization of potential projects

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: MARCH 2025

CURRENT PHASE: INITIAL STUDY

EST. COMPLETION DATE: TBD

PROJECT MANAGER: TIM JOHNSON, PE

PARKS MASTER PLAN

PARKS, RECREATION & CULTURAL RESOURCES



START DATE: TBD

CURRENT PHASE: DESIGN

EST. COMPLETION DATE: LATE 2026

PROJECT MANAGER: KYLE COOPER

SUMMARY

Update the 2018 Parks, Recreation & Cultural Resources Master Plan based on current and future community needs in accordance with the Commission for Accreditation of Park and Recreation Agencies (CAPRA) standards and recreational requirements.

STATUS

- The Town advertised a Parks Master Plan Request for Qualifications to solicit consultant firms to engage with the Town on this project.
- Interviews with the top ranked firms have been completed, the most qualified firm has been selected, and Town staff are negotiating a scope of work and fee proposal with the top ranked firm.

Challenges:

FINANCES

Total Revenues & Sources
\$200,000

Latest Indicated Cost
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

INTERSECTION IMPROVEMENTS - FUTURE



SUMMARY

In 2021 the Town conducted an intersection improvement study. In January 2022 Town Council adopted a phased approach to implementing the recommended intersection improvements. In coordination with the current update to the Town's Comprehensive Transportation Plan, the intersection improvement study will also be updated.

STATUS

- A consultant has been selected for the Comprehensive Transportation Plan (CTP) update and the process is anticipated to run through October of 2026.
- The CTP will provide an update to the previous plan developed in 2021
- Future intersection improvement projects are programmed for design and implementation starting in FY27.

FINANCES

Total Revenues & Sources
\$2.2 million

Latest Indicated Cost
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: FUTURE FY27

CURRENT PHASE: STUDY

EST. COMPLETION DATE: TBD

PROJECT MANAGER: TBD

COMMUNITY CENTER



SUMMARY

Community, recreation and senior center facility development in conjunction with Town Center future phases. Large scale facility including a parking deck to provide amenities such as in-door basketball, pickleball, volleyball and fitness/educational classes for all ages and abilities.

STATUS

- A community center was proposed as part of the land use plan development in 2018 for the Town Center District Area.
- This project will require substantial investment upwards of \$40 - \$50 million dollars.

FINANCES

Total Revenues & Sources
\$TBD

Latest Indicated Cost - Design + Construction
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

START DATE: FY30

CURRENT PHASE: PLANNING

EST. COMPLETION DATE: TBD

PROJECT MANAGER: TBD

MARCOM DRIVE PARKLAND

PARKS, RECREATION & CULTURAL RESOURCES



START DATE: FY 30

CURRENT PHASE: FUTURE PROJECT

EST. COMPLETION DATE: TBD

PROJECT MANAGER: KYLE COOPER

SUMMARY

Future park site on Town owned property located near the intersection of Sorrell Grove Church Road and Marcom Drive north of Airport Blvd. Encompasses 9 acres of Town owned land with a possible partnership with Wake County owned land and a stormwater control lake for recreational use.

STATUS

- This is a future park project. It is dependent on additional land acquisition and coordination with Wake County.
- Programming will be determined as part of the parks master plan development.

FINANCES

Total Revenues & Sources
\$5,900,000 (FY 30)

Latest Indicated Cost
\$TBD

STRATEGIC PLAN

- Sustainable, livable community growth
- Public safety readiness
- Engaged, inclusive community
- Community mobility
- Economic prosperity
- Operational excellence
- Organizational resiliency

GLOSSARY



ADA Compliance - Ensures that individuals with disabilities have equal access to services, facilities, and information. American Disabilities Act (ADA) is federal law that prohibits discrimination against people with disabilities in various areas, including employment, public accommodations, transportation, and telecommunications. Compliance means making reasonable modifications and adjustments to policies, practices, and procedures to accommodate individuals with disabilities.

ARPA Funds - American Rescue Plan Act (ARPA) provided to local and tribal governments for COVID-19 recovery efforts. These funds can be used for a wide range of purposes, including offsetting revenue losses, addressing pandemic impacts, providing premium pay for essential workers, and investing in infrastructure.

CDs – Construction Drawings or Construction Documents are plans/blueprints developed during the design phase of the project.

DEQ – The North Carolina Department of Environmental Quality (DEQ)

Easement Acquisition- the process of acquiring a right to use another person's property for a specific purpose, without taking ownership of the land itself. This can involve negotiating and obtaining an agreement with the property owner for the right to use the land generally for the development of infrastructure projects.

Public Private Partnership- is a cooperative arrangement between a government and a private company to deliver a public service, facility, park, housing or infrastructure project. These partnerships aim to leverage private sector expertise, funding, and innovation to enhance the efficiency, quality, and cost-effectiveness of the public improvements.

GLOSSARY



Right(s) of Way - is a specific public route taken by people, animals, vehicles, watercraft, or where utility lines travel and gives them the legal right to do so. Rights-of-way in the physical sense include public highways, roadways, sidewalks, railroads, streams, hiking paths/greenways, multi-use paths/bicycle paths and utility corridors.

Site Plan - also known as a plot plan, is a detailed drawing that shows the layout and features of a construction site or a property. It's essentially a blueprint for how a building or development fits within its surroundings, including existing and proposed structures, infrastructure, and landscaping.

Special Use Permit - allows activities on land that are generally not permitted by zoning regulations but are allowed under specific conditions. Essentially, it's a permission slip for land use that would otherwise be prohibited but may be allowed with special permission and approvals.

LAPP Funding - The Locally Administered Projects Program (LAPP) was first adopted by the NC Capital Area MPO on October 20, 2010. The program is used by the MPO to prioritize and program local transportation projects in the region that utilize federal funding. LAPP is a competitive funding program managed by CAMPO that prioritizes locally administered projects in the Region. These projects are funded using federal funding sources directly attributed to the region with a minimum 20% local match. The Town of Morrisville is a member jurisdiction of the CAMPO region and is eligible to apply for these funds.

STIP - The N.C. Department of Transportation's long-range transportation plan – called the State Transportation Improvement Program (STIP) – identifies the construction funding and schedule for state transportation projects over a 10-year period. NCDOT updates the STIP approximately every two years.

GLOSSARY



Streets PIL (Payment in Lieu) – means instead of or as a substitute for payment. Streets PIL are payments collected by the Town for private development that will require future road construction in lieu of constructing the road as part of the development.

Traffic Warrant – A traffic engineering analysis using collected data to determine whether or not a certain construction improvement meets the required standards for implementation. For example, the installation of a new traffic signal requires a warrant analysis to determine if a new signal installation meets the minimum criteria and will provide an engineering/safety benefit if installed. Warrants study vehicle volume data, turning movement data and crash data to make a determination.

Let a project - In the construction industry, the term “letting” refers to the process of awarding contracts for construction projects through a formal bidding process. This phase is essentially the official construction commencement date.

Parks PIL (Payment in Lieu) - means instead of or as a substitute for payment. Parks PIL are payments collected by the Town for private development that will require future park construction in lieu of constructing the park as part of the development.

NCDOT - stands for North Carolina Department of Transportation. It's the state agency responsible for managing and operating various transportation systems within North Carolina, including highways, rail, aviation, and public transit. NCDOT is responsible for ensuring the safety, efficiency, and accessibility of transportation infrastructure across the state on the state-maintained right-of-way network.

CAMPO (Capital Area Metropolitan Planning Organization) - a regional transportation planning organization serving communities in Chatham, Franklin, Granville, Harnett, Johnston and Wake Counties.

